

DAVID J. MEYER
VICE PRESIDENT AND CHIEF COUNSEL FOR
REGULATORY & GOVERNMENTAL AFFAIRS
AVISTA CORPORATION
P.O. BOX 3727
1411 EAST MISSION AVENUE
SPOKANE, WASHINGTON 99220-3727
TELEPHONE: (509) 495-4316
FACSIMILE: (509) 495-8851
DAVID.MEYER@AVISTACORP.COM

BEFORE THE IDAHO PUBLIC UTILITIES COMMISSION

IN THE MATTER OF THE APPLICATION)	CASE NO. AVU-E-15-05
OF AVISTA CORPORATION FOR THE)	CASE NO. AVU-G-15-01
AUTHORITY TO INCREASE ITS RATES)	
AND CHARGES FOR ELECTRIC AND)	
NATURAL GAS SERVICE TO ELECTRIC)	EXHIBIT NO. 8
AND NATURAL GAS CUSTOMERS IN THE)	
STATE OF IDAHO)	DON F. KOPCZYNSKI
_____)	

FOR AVISTA CORPORATION

(ELECTRIC AND NATURAL GAS)

Customer Usage
State of Idaho - Electric & Natural Gas
As of December 31, 2014

Electric			kWh	
	Schedule	No. of Customers	(000s)	% of Total kWh
	Residential Sch. 1	103,747	1,150,635	37%
	General Sch. 11&12	20,669	364,778	12%
	Lg. General Sch. 21&22	1,156	700,678	23%
	Ex. Lg. General Sch. 25&25P	10	791,161	26%
	Pumping Sch. 30,31&32	1,406	58,840	2%
	Street & Area Lights	146	13,588	0%
		127,134	3,079,680	100%

Natural Gas			Therms	
	Schedule	No. of Customers	(000s)	% of Total Therms
	General Service 101	76,642	54,234	46%
	Lg. General Service 111&112	1,411	22,432	19%
	Interruptible Service 132	1	330	0%
	Transportation Service & Other	7	40,738	35%
		78,061	117,734	100%

Total Electric & Gas Customers	205,195
---	---------

Gas Facilities Replacement Program (GFRP) Aldyl A Pipe Replacement Update

Prepared for:
Idaho Public Utilities Commission

January 20, 2015

IDAHO (SYSTEM WIDE QUANTITIES AT 2012 PROGRAM START)		
	MAIN PIPE (MILES)	STTR'S (UNITS)
QUANTITIES	131	3152
% OF SYSTEM	18%	18%

GAS FACILITY		
IDAHO		
YEAR	MAIN PIPE (MILES)	STTR'S (UNITS)
2013	0.0	400
2014	3.4	625
2015	3.5	625
2016	3.6	625
2017	3.7	625

2015 MAIN PIPE REPLACEMENT PROJECTS

LOCATION	GENERAL DESCRIPTION	PUC COMMITTED	START	END
POST FALLS EAST POST FALLS, ID	3.65 - ALDYL A MAIN PIPE REPLACEMENT	3.5 MILES	MAY	NOVEMBER
	CPC: BRIAN ZEMKE			

2015 SERVICE TEE TRANSITION REBUILD (STTR) PROJECTS

LOCATIONS	GENERAL DESCRIPTION	PUC COMMITTED	START	END
LEWISTON, ID	REBUILD APPROX. 734 ALDYL A STTR UNITS	625 UNITS	FEBRUARY	MAY
	CPC: KEN WUESTHOFF			


IDAHO - GFRP/ALDYL A PIPE REPLACEMENT PERFORMANCE SUMMARY 2012 - 2014

GFRP PROGRAM YEAR	PLANNED MAIN	COMPLETED MAIN	PLANNED STTR	COMPLETED STTR
2012	0	0	0	0
2013	0	0	400	253
2014	3.42	3.65	625	933*
TOTAL	3.42	3.65	1025	1186

* STTR QUANTITIES EXCEEDED PRIMARILY DUE TO THE QUANTITY OF UNITS REQUIRING MAP CORRECTION IN LIEU OF CONSTRUCTION REBUILDS.

Michael Whitby, GFRP Project Manager
michael.whitby@avistacorp.com
 509-495-4261

2015 Post Falls Main Pipe Replacement Project Map

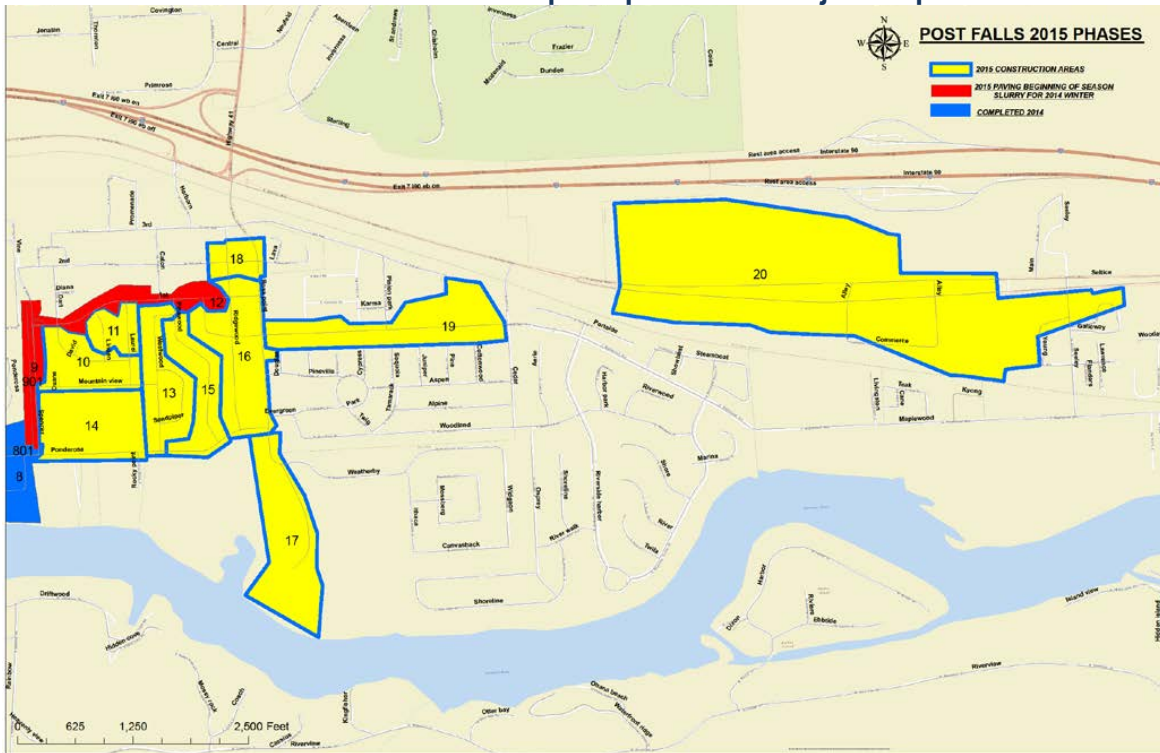

2015 Lewiston, ID STTR Project Overview Map

